Welcome

COURSE:
ADVANCED PROJECT MANAGEMENT IN AI

Lesson 1 Session 1

Understanding AI Projects

欢迎

课程：
人工智能高级项目管理

第 1 课 第 1 节

理解人工智能项目

Prof Divya Nambiar



Divya Nambiar教授



Introduction of the Professor

- I am originally from India, now settled in Canada.

- Professor of Project Management, Strategic Management, Risk and Innovation management

- Master’s degree in Project Management and professional certifications, including Professional Scrum Master and Project Management Professional (PMP).

教授简介

- 我来自印度，现定居加拿大。
- 项目管理、战略管理、风险与创新管理教授
- 持有项目管理硕士学位及专业认证，包括专业敏捷教练和项目管理专业人士（PMP）。

Introduction of the Professor

- 14 years of teaching experience

- 17 years of experience as a practitioner

- My academic and professional work focuses on understanding how organizations design and manage complex strategic initiatives, particularly those involving project management, strategic transformation, and heavily emerging technologies such as **Artificial Intelligence**.

- Contributor to the development of international, keynote speaker

教授简介

- 14 年教学经验
- 17 年从业经验
- 我的学术与专业研究致力于探究组织如何设计并管理复杂战略项目，尤其聚焦项目管理、战略转型以及**人工智能**等前沿技术深度应用的相关项目。
- 国际标准制定参与者，主旨演讲嘉宾

Course Presentation

- Lesson 1: Foundations of AI Project Management
- Lesson 2: Planning and Scheduling AI Projects
- Lesson 3: Resource Management in AI Projects
- Lesson 4: Risk Management in AI Projects
- Lesson 5: Agile and Team Management in AI Projects
- Lesson 6: Monitoring, Quality Assurance, and Case Studies

课程概述

- 第 1 课：人工智能项目管理基础
- 第 2 课：人工智能项目规划与进度安排
- 第 3 课：人工智能项目资源管理
- 第 4 课：人工智能项目风险管理
- 第 5 课：人工智能项目敏捷与团队管理
- 第 6 课：监控、质量保证及案例分析

LESSON 1.1 – Nature of AI Projects



第 1.1 节 人工智能项目的本质



2. Learning Objectives: Lesson 1.1

- Distinguish AI projects from traditional IT projects
- Explain the experimental nature of AI systems
- Identify key characteristics that influence AI project management
- Recognize uncertainty and data dependency as core structural factors

2. 学习目标：第 1.1 节

- 区分人工智能项目与传统信息技术项目
- 阐释人工智能系统的实验性特征
- 识别影响人工智能项目管理的关键特征
- 认识不确定性与数据依赖性为核心结构性因素

What Is an AI Project?

An AI project involves the development, training, validation, and deployment of systems that learn patterns from data to perform predictive or decision-making tasks.

Examples:

Fraud detection systems

Medical diagnosis models

Recommendation engines

Predictive maintenance systems



Russell, S., & Norvig, P. (2021). *Artificial Intelligence: A Modern Approach* (4th ed.). Pearson.

什么是人工智能项目?

人工智能项目涉及对从数据中学习模式以执行预测或决策任务的系统进行开发、训练、验证与部署。

示例：

欺诈检测系统

医学诊断模型


推荐引擎

预测性维护系统



拉塞尔，S.，诺维格，P.（2021）. *人工智能：一种现代方法（第 4 版）*. 培生教育出版集团。


Examples of AI Projects Across Industries



- Healthcare – AI-assisted medical imaging for early disease detection
- Finance – real-time fraud detection and credit risk analysis
- Retail & E-commerce – recommendation systems and demand forecasting
- Transportation & logistics – route optimization and

  predictive maintenance

各行业人工智能项目示例



- 医疗保健 —— 用于疾病早期检测的人工智能辅助医学影像
- 金融 —— 实时欺诈检测与信用风险分析
- 零售与电子商务 —— 推荐系统与需求预测
- 运输与物流 —— 路线优化与预测性维护

Why Organizations Are Investing in AI?

- Analyze large volumes of data and uncover valuable insights.
- Identify patterns and relationships that may be difficult for humans to detect using traditional analysis methods.
- Automate complex decision-support tasks, improving both speed and consistency in organizational processes.
- Key driver of innovation, productivity, and long-term competitive advantage.

Davenport, T. H., & Ronanki, R. (2018). Artificial intelligence for the real world. *Harvard Business Review*, 96(1), 108–116.

企业为何投资人工智能?

- 分析海量数据并挖掘有价值的洞察。
- 识别人类借助传统分析方法难以发现的模式与关联。
- 自动化复杂的决策支持任务，提升企业流程的效率与一致性。
- 创新、生产力及长期竞争优势的核心驱动力

达文波特，T. H.，罗南基，R.（2018）. 现实世界中的人工智能 . *哈佛商业评论*，96（1），108–116.

AI Projects vs Traditional Tech Projects

- Traditional software systems rely on deterministic logic (system always produces the same output when given the same input)
- AI systems, by contrast, typically produce **probabilistic outputs** based on patterns learned from data.

  For example, an AI model might estimate the probability that a transaction is fraudulent rather than providing a simple yes-or-no rule.
- AI projects often involve experimentation and iterative improvement, because models must be trained and refined using data.

These characteristics make AI projects more uncertain and exploratory than conventional software development initiatives.

人工智能项目与传统技术项目对比

- 传统软件系统依赖确定性逻辑（相同输入始终产生相同输出）
- 相比之下，人工智能系统通常基于从数据中学习的模式生成概率性输出。

  例如，人工智能模型可能估算一笔交易存在欺诈的概率，而非给出简单的是或否判断。



- 人工智能项目往往涉及实验与迭代优化，因为模型需通过数据进行训练与完善。

这些特征使得人工智能项目比传统软件开发项目更具不确定性与探索性。

Core Components of an AI Project



Data
The dataset used to train and evaluate the model.



Algorithms
Mathematical methods used to identify patterns in the data.



Computing Infrastructure
Processing resources required to train and deploy AI models.

Successful AI systems depend heavily on data availability, data quality, and appropriate computational resources.

人工智能项目的核心构成



数据
用于训练与评估模型的数据集。




算法
用于识别数据中模式的数学方法。



计算基础设施
训练和部署人工智能模型所需的处理资源。

成功的人工智能系统高度依赖数据可得性、数据质量以及合适的计算资源。

The AI Project Lifecycle

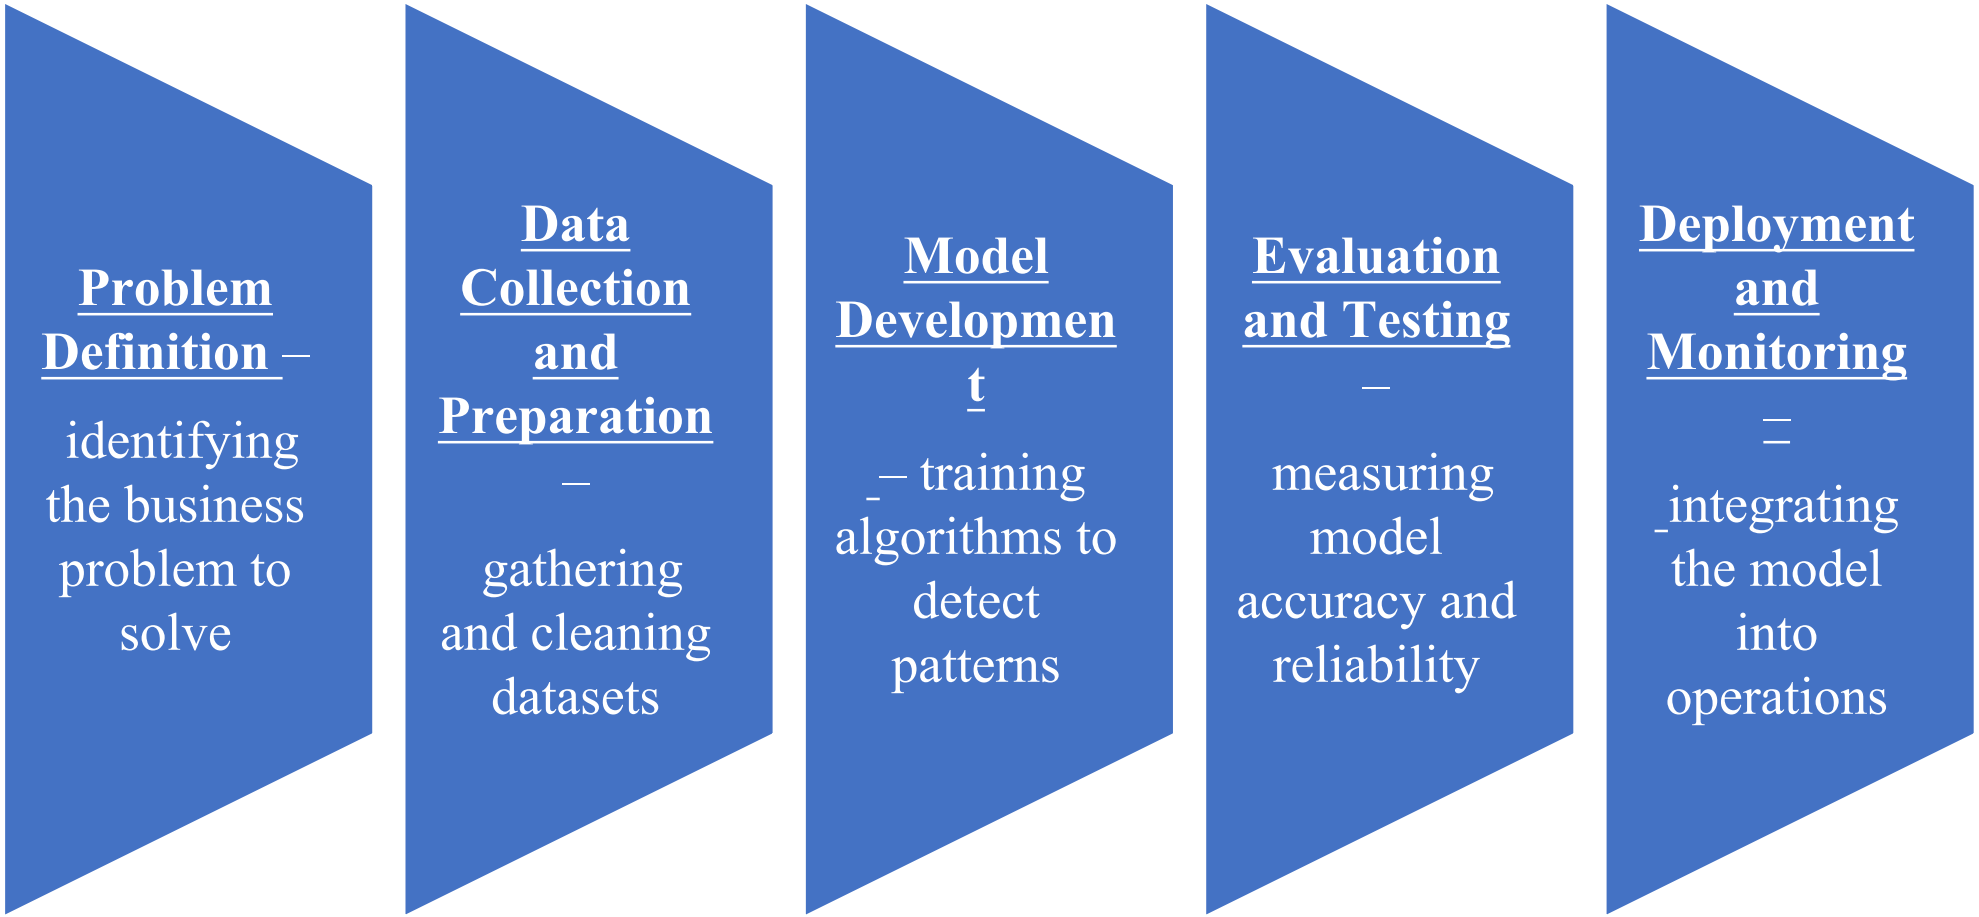

人工智能项目生命周期

问题定义 –

明确待解决的业务问题

数据收集与预处理 –

采集并清洗数据集

模型开发 –

训练算法以识别数据模式

评估与测试 –

衡量模型的准确性与可靠性

部署与监控 –

将模型集成至业务运营流程

The Role of Data in AI Projects

- Data is the fundamental resource that enables AI systems to learn and improve.
- Effective AI models depend on three important characteristics of data:
  - Quality – accuracy and reliability of the dataset
  - Volume – sufficient data to identify meaningful patterns
  - Diversity – representation of different real-world scenarios

Poor or biased data can lead to inaccurate predictions or unintended outcomes, making data governance a critical aspect of AI project management.

Domingos, P. (2015). The Master Algorithm. Basic Books.

数据在人工智能项目中的作用

- 数据是支撑人工智能系统学习与优化的核心资源。
- 高效的人工智能模型依赖数据的三大重要特征：
  - 质量 —— 数据集的准确性与可靠性
  - 体量 —— 足以识别有效模式的充足数据量
  - 多样性 —— 对不同现实场景的覆盖与代表性

劣质或带有偏见的数据会导致预测失准或非预期结果，因此数据治理成为人工智能项目管理的关键环节。

多明戈斯，P.（2015）. 终极算法. 基础图书出版社。

Risks and Challenges in AI Projects



- AI projects face several technical and organizational challenges.
- Common risks include:
  - Poor data quality or insufficient data availability
  - Unclear problem definition or unrealistic expectations
  - Ethical concerns such as algorithmic bias
  - Difficulties integrating AI systems into existing workflows

These challenges mean that successful AI implementation requires not only technical expertise but also effective management and organizational readiness

人工智能项目的风险与挑战



- 人工智能项目面临若干技术与组织层面的挑战。
- 常见风险包括：
  - 数据质量低下或数据可得性不足
  - 问题定义不清晰或预期不切实际
  - 算法偏见等伦理问题
  - 将人工智能系统集成至现有工作流程的困难

这些挑战意味着，人工智能的成功落地不仅需要专业技术能力，还需要高效的管理与组织层面的准备。

Mini Case: AI in Healthcare – Detecting Diabetic Retinopathy

Deep learning model to detect diabetic retinopathy, (a major cause of preventable blindness)

- Trained on over 100,000 retinal images
- Able to identify signs of the disease with accuracy comparable to trained ophthalmologists.
- Improving early diagnosis and expanding access to screening

This case also highlights the importance of large, high-quality datasets and rigorous validation in real-world AI projects.

Gulshan, V., et al. (2016). Development and validation of a deep learning algorithm for detection of diabetic retinopathy. *JAMA*, 316(22), 2402–2410.

迷你案例：医疗领域人工智能 —— 糖尿病视网膜病变检测

用于检测糖尿病视网膜病变（可预防性失明的主要诱因）的深度学习模型

- 基于超 10 万张视网膜图像进行训练
- 能够识别疾病征兆，准确率与专业眼科医师相当
- 提升早期诊断水平并扩大筛查覆盖面

该案例同时凸显了大规模高质量数据集与严格验证在现实人工智能项目中的重要性。

古尔沙恩，V. 等（2016）.用于检测糖尿病视网膜病变的深度学习算法的开发与验证.*美国医学会杂志*，316（22），2402–2410.

Reflection Exercise



Consider an organization or industry you are familiar with.

Question

Where could AI potentially be used to improve decision-making or efficiency?

Think about:

- What problem could AI help solve?
  - What type of data might be required?
  - What challenges might arise in implementing such a system?

Take a moment to reflect before continuing.

反思练习



思考一个你熟悉的组织或行业。

问题

人工智能可在哪些方面用于优化决策或提升效率？

思考要点：

- 人工智能可帮助解决什么问题？
  - 需要何种类型的数据？
  - 实施该系统可能面临哪些挑战？

请先进行思考，再继续后续内容。

Why AI Projects Require New Management Approaches

- AI projects often involve uncertainty, experimentation, and interdisciplinary collaboration.
- Teams may include data scientists, software engineers, domain experts, and business stakeholders, each contributing different expertise.
- Project managers must therefore coordinate diverse perspectives while ensuring that technical development aligns with organizational goals and practical constraints.

- Successful AI project management requires flexibility, clear communication, and a strong understanding of both business and technological contexts.

人工智能项目为何需要全新的管理方法

- 人工智能项目通常涉及不确定性、实验性与跨学科协作。
- 团队成员可能包括数据科学家、软件工程师、领域专家及业务相关方，各自具备不同专业能力。
- 因此，项目经理必须协调多元视角，同时确保技术开发与组织目标及实际约束相契合。

- 成功的人工智能项目管理需要灵活性、清晰的沟通，以及对业务与技术环境的深刻理解。

Key Takeaways

1. AI projects involve developing systems that use data and algorithms to perform tasks associated with human intelligence, such as recognizing patterns or making predictions.
2. Unlike traditional software systems, AI models produce probabilistic outcomes based on learned patterns, which introduces additional uncertainty into project development.
3. Successful AI initiatives depend on high-quality data, appropriate algorithms, and effective interdisciplinary collaboration.
4. Understanding these characteristics is essential for managers who aim to plan, implement, and evaluate AI-driven initiatives effectively.

核心要点

1. 人工智能项目涉及开发利用数据和算法执行与人类智能相关任务的系统，例如模式识别或预测。
2. 与传统软件系统不同，人工智能模型基于学习到的模式生成概率性结果，这为项目开发带来了额外的不确定性。
3. 成功的人工智能项目依赖高质量数据、合适的算法以及高效的跨学科协作。
4. 理解这些特征，对于旨在有效规划、实施与评估人工智能驱动项目的管理者而言至关重要。

THANKS !!!



谢谢 !!!



Welcome

COURSE:
ADVANCED PROJECT MANAGEMENT IN AI

Lesson 1 Session 2

Understanding AI Projects:
Project Management Principles
in AI Contexts

欢迎

课程：
人工智能高级项目管理

第 1 课 第 2 节

理解人工智能项目：
人工智能场景下的项目管理原则

LESSON 1.2 – Project Management Principles in AI Contexts



第 1.2 节 人工智能场景下的项目管理原则



2. Learning Objectives: Lesson 1.2

- Explain how traditional project management knowledge areas apply to AI initiatives.
- Identify unique challenges AI projects introduce in scope, time, cost, quality, risk, and stakeholder management.
- Describe why AI projects often require iterative planning and flexibility.
- Recognize the importance of ethical, social, and regulatory considerations in AI project management.

2. 学习目标：第 1.2 节

- 阐释传统项目管理知识领域如何应用于人工智能项目。
- 识别人工智能项目在范围、时间、成本、质量、风险及相关方管理中带来的独特挑战。
- 说明人工智能项目为何通常需要迭代规划与灵活性。
- 认识伦理、社会及法规考量在人工智能项目管理中的重要性。

Project Management Foundations

AI initiatives are still managed using core project management knowledge areas:

- Scope management
- Schedule (time) management
- Cost management
- Quality management
- Risk management
- Stakeholder management



PMI PMBOK Guide

项目管理基础

人工智能项目仍需运用项目管理核心知识领域进行管理：

- 范围管理
- 进度（时间）管理
- 成本管理
- 质量管理
- 风险管理
- 相关方管理



项目管理协会《项目管理知识体系指南》

Project Delivery Approaches



Projects may follow different development approaches:

Waterfall: Sequential development phases; suitable when requirements are stable

Agile: Iterative development and continuous feedback

Hybrid: Structured planning combined with iterative development

AI projects typically require greater flexibility and experimentation

项目交付方式



项目可采用不同的开发方式：

瀑布式： 分阶段顺序开发；适用于需求稳定的场景

敏捷式： 迭代开发与持续反馈

混合式： 结构化规划结合迭代开发

人工智能项目通常需要更高的灵活性与实验性。

Why AI Challenges Traditional Planning?

AI initiatives introduce several sources of uncertainty:

- Evolving problem definitions
- Dependence on large datasets
- Probabilistic outcomes rather than deterministic outputs
- Experimentation with multiple models

Project management must support
learning and discovery, not just execution

人工智能为何对传统规划构成挑战?

人工智能项目带来多重不确定性来源：

- 问题定义不断演变
- 依赖大规模数据集
- 概率性输出而非确定性结果
- 多模型实验验证

项目管理必须支撑

学习与探索，而非仅关注执行。

Scope Management in AI Projects

Traditional scope management: Define requirements and control changes



AI scope management: Evolves as teams:

- Explore available datasets
- Test different machine learning models
- Refine features and variables

Example:
A company predicting customer churn may start with transaction history, then integrate customer service interactions and usage data as insights emerge.

人工智能项目的范围管理

传统范围管理：

定义需求并控制变更




人工智能范围管理：随着团队开展以下工作而动态演进：

- 探索现有数据集
- 测试不同机器学习模型
- 优化特征与变量

示例：
一家预测客户流失的企业，初期可采用交易记录数据，随着研究深入，再整合客服交互数据与使用行为数据。

Time Management in AI Projects

Traditional: Predictable development tasks




AI: Iterative experimentation

- Model training cycles
- Algorithm tuning
- Validation and testing

Example:
A hospital developing an AI tumor detection system may need to train several models and test thousands of images before reaching acceptable accuracy.

人工智能项目的时间管理

传统项目： 开发任务可预测




人工智能：迭代式实验

- 模型训练周期
- 算法调优
- 验证与测试

示例：
某医院开发人工智能肿瘤检测系统，可能需要训练多个模型、测试数千张图像，才能达到可接受的准确率。

Cost Management in AI Projects

AI-specific cost drivers:




- Data acquisition and labeling
- Specialized AI expertise
- Cloud computing infrastructure
- Large-scale model training

Example:
A streaming platform training a recommendation system must process millions of interactions daily, requiring substantial cloud storage and computing resources.

人工智能项目的成本管理

人工智能特有成本驱动因素：



- 数据采集与标注
- 专业人工智能人才
- 云计算基础设施
- 大规模模型训练

示例：

某流媒体平台训练推荐系统，每日需处理数百万次交互行为，需要大量云存储与计算资源。

Quality Management in AI Projects

Considerations beyond functional specs:



- Model accuracy and reliability
- Fairness and bias mitigation
- Robustness to changing data
- Transparency and explainability

Example:
An automated hiring tool trained on historical data may systematically disadvantage certain applicants if past bias is present.

人工智能项目的质量管理

超越功能规格的考量因素：


- 模型准确性与可靠性
- 公平性与偏见缓解
- 数据变化时的鲁棒性
- 透明度与可解释性



示例：
基于历史数据训练的自动化招聘工具，若历史数据存在偏见，可能会系统性地对特定申请者造成不利影响。

Risk Management in AI Projects

AI-specific risks:




- Algorithmic bias
- Model drift over time
- Data privacy concerns
- Regulatory compliance challenges

Example:
A credit approval AI trained on historical lending data may reproduce discriminatory practices, exposing the organization to legal and reputational risks.

人工智能项目的风险管理

人工智能特有风险：



- 算法偏见
- 模型随时间漂移
- 数据隐私问题
- 法规合规挑战

示例：
基于历史借贷数据训练的信贷审批人工智能，可能会复刻歧视性做法，使组织面临法律与声誉风险。

Stakeholder Management in AI Projects

Broader stakeholder considerations:

- Technical teams and engineers
- Business decision makers
- Regulators and policymakers
- Individuals affected by automated decisions



Example:
A city deploying facial recognition technology must consider engineers, city officials, civil liberties groups, and the public concerned about privacy.

人工智能项目的相关方管理

更广泛的相关方考量：

- 技术团队与工程师
- 业务决策者
- 监管机构与政策制定者
- 受自动化决策影响的个体



示例：

部署人脸识别技术的城市，必须考虑工程师、市政官员、公民自由组织以及关注隐私的公众。

Key Takeaways

- Traditional project management principles remain relevant but require adaptation for AI projects.
- AI initiatives demand iterative planning, evolving scope, and a strong focus on data quality and model reliability.
- Risk and stakeholder management must include ethical, social, and regulatory considerations.
- Successful AI project management balances technical expertise, experimentation, and responsible decision-making.

核心要点

- 传统项目管理原则依然适用，但需针对人工智能项目进行调整。
- 人工智能项目要求迭代规划、动态范围，并高度关注数据质量与模型可靠性。
- 风险与相关方管理必须纳入伦理、社会及法规层面的考量。
- 成功的人工智能项目管理需平衡专业技术、实验探索与负责任的决策。

THANKS !!!



谢谢 !!!



Welcome

COURSE:
ADVANCED PROJECT MANAGEMENT IN AI

Lesson 1 Session 3

Understanding AI Projects:
AI Project Success Criteria

欢迎

课程：
人工智能高级项目管理

第 1 课 第 3 节

理解人工智能项目：
人工智能项目成功标准

LESSON 1.3 – AI Project Success Criteria



第 1.3 节 人工智能项目成功标准



2. Learning Objectives: Lesson 1.3

- Distinguish technical model performance from business value outcomes
- Evaluate model accuracy versus deployment success
- Identify adoption and operational metrics used to measure AI impact
- Recognize ethical and regulatory compliance as success factors
- Understand how organizational AI maturity influences success criteria

2. 学习目标：第 1.3 节

- 区分技术模型性能与业务价值成果
- 评估模型准确率与部署成功度
- 识别人工智能影响衡量所采用的采纳度与运营指标
- 将伦理与法规合规视为成功因素
- 理解组织人工智能成熟度如何影响成功标准

Technical Performance vs Business Value

AI development often focuses on technical evaluation metrics, but organizations evaluate business outcomes.

Technical metrics

- Accuracy
- Precision / recall
- F1 score
- Prediction latency

Example
- A recommendation model improves prediction accuracy but fails to increase customer purchases.

Business metrics

- Revenue increase
- Customer retention improvement
- Cost reduction
- Faster decision cycles

技术性能与业务价值

人工智能开发通常聚焦技术评估指标，而组织则以业务成果为评判标准。

技术指标

- 准确率
- 精确率 / 召回率
- F1 分数
- 预测延迟

业务指标

- 收入增长
- 客户留存提升
- 成本降低
- 决策周期缩短

示例

- 某推荐模型提升了预测准确率，却未能带动客户购买量增长。

Model Accuracy vs Deployment Success

Models that perform well in testing may fail when deployed in real environments.

Deployment success depends on:

- Integration with production systems
- Real-time inference capability
- Monitoring and retraining pipelines
- Reliability and scalability

Examples
- Fraud detection model produces excessive false positives
- Medical AI trained on curated data struggles with real-world clinical data

Lewis, G. A., Bellomo, S., & Ozkaya, I. (2021). *Characterizing and detecting mismatch in machine-learning-enabled systems.* Carnegie Mellon Software Engineering Institute.

模型准确率与部署成功度

测试中表现良好的模型，在实际环境部署时可能失效。

部署成功取决于：

- 与生产系统的集成
- 实时推理能力
- 监控与再训练流程
- 可靠性与可扩展性

示例
- 欺诈检测模型产生过多误报
- 基于精选数据训练的医疗人工智能在真实临床数据中表现不佳

刘易斯，G. A.，贝洛莫，S.，& 奥兹卡亚，I.（2021）. *机器学习系统中不匹配的特征描述与检测*. 卡内基梅隆大学软件工程研究所.

Adoption and Usage Metrics

AI generates value only when users trust and adopt the system.

Adoption indicators:

- Percentage of decisions supported by AI
- Active user adoption rate
- Frequency of AI recommendation usage
- User satisfaction or trust scores

Examples
- Sales teams follow AI-generated leads in a majority of cases
- Clinicians incorporate AI diagnostic support into routine assessments

采纳度与使用指标

人工智能只有在用户信任并采纳系统时才能创造价值。

采纳度指标：

- 人工智能辅助决策占比
- 活跃用户采纳率
- 人工智能建议使用频率
- 用户满意度或信任度评分

示例

- 销售团队在多数情况下采纳人工智能生成的销售线索
- 临床医生将人工智能诊断辅助纳入常规评估流程

Operational Impact Metrics

AI projects often create value through process improvements.

Operational metrics:

- Reduction in process completion time
- Error rate reduction
- Automation of manual tasks
- System reliability and uptime

Examples
- AI document processing reduces loan approval time from days to hours
- Predictive maintenance reduces manufacturing downtime

运营影响指标

人工智能项目通常通过流程优化创造价值。

运营指标：

- 流程完成时间缩短
- 错误率降低
- 手动任务自动化
- 系统可靠性与正常运行时间

示例

- 人工智能文档处理将贷款审批时间从天级缩短至小时级
- 预测性维护减少制造业停机时间

Ethical, Governance, and Regulatory Success Factors

Responsible AI deployment is now a key success criterion.

Governance indicators:

- Algorithmic fairness and bias mitigation
- Data privacy protection
- Model transparency and explainability
- Compliance with regulatory requirements

Example:

- Credit scoring systems must comply with fair lending laws
- Healthcare AI must meet clinical safety and regulatory standards

National Institute of Standards and Technology. (2023). *Artificial Intelligence Risk Management Framework (AI RMF 1.0).*

伦理、治理与法规合规成功因素

负责任的人工智能部署已成为关键成功标准。

治理指标：

- 算法公平性与偏见缓解
- 数据隐私保护
- 模型透明度与可解释性
- 合规法规要求

示例：

- 信用评分系统必须遵守公平借贷法律
- 医疗人工智能必须符合临床安全与监管标准

美国国家标准与技术研究院. (2023). *人工智能风险管理框架（AI RMF 1.0）*.

Defining Success in AI Projects

AI project success is multi-dimensional and includes:

- Technical performance — model accuracy, precision, recall
- Business value — revenue growth, cost reduction, improved decisions
- Operational performance — process efficiency improvements
- User adoption — integration into decision workflows
- Responsible AI compliance — fairness, transparency, privacy

Example
A demand forecasting model may achieve high predictive accuracy, but success is measured by inventory optimization and improved supply chain efficiency.

Amershi, S., Begel, A., Bird, C., DeLine, R., Gall, H., Kamar, E., Nagappan, N., Nushi, B., & Zimmermann, T. (2019). *Software engineering for machine learning: A case study.* Proceedings of the 41st International Conference on Software Engineering.

人工智能项目的成功定义

人工智能项目的成功具有多维度，包括：

- 技术性能 —— 模型准确率、精确率、召回率
- 业务价值 —— 收入增长、成本降低、决策优化
- 运营绩效 —— 流程效率提升
- 用户采纳 —— 融入决策工作流程
- 负责任人工智能合规 —— 公平性、透明度、隐私

示例
某需求预测模型可能达到很高的预测准确率，但其成功需通过库存优化与供应链效率提升来衡量。

阿默希，S.，贝盖勒，A.，伯德，C.，德莱恩，R.，加尔，H.，卡马尔，E.，纳加潘，N.，努希，B.，& 齐默尔曼，T.（2019）. *面向机器学习的软件工程：案例研究*. 第 41 届国际软件工程大会论文集.

Key Takeaways

- AI project success extends beyond model accuracy.
- Success must include deployment success, adoption, operational impact, and financial value.
- Responsible AI governance is increasingly essential.
- Success criteria should align with organizational maturity and business objectives.

核心要点

- 人工智能项目的成功远不止模型准确率。
- 成功必须包含部署成效、用户采纳、运营影响与财务价值。
- 负责任的人工智能治理愈发重要。
- 成功标准应与组织成熟度及业务目标保持一致。

THANKS !!!



谢谢 !!!

